


Horz. Stab troubles



The plans show a .875 difference in length between the horz. stab TE and elevator LE so that's how they were built. Unfortunately the plans are wrong as this makes the LE too short to properly mount the elevator control horn .

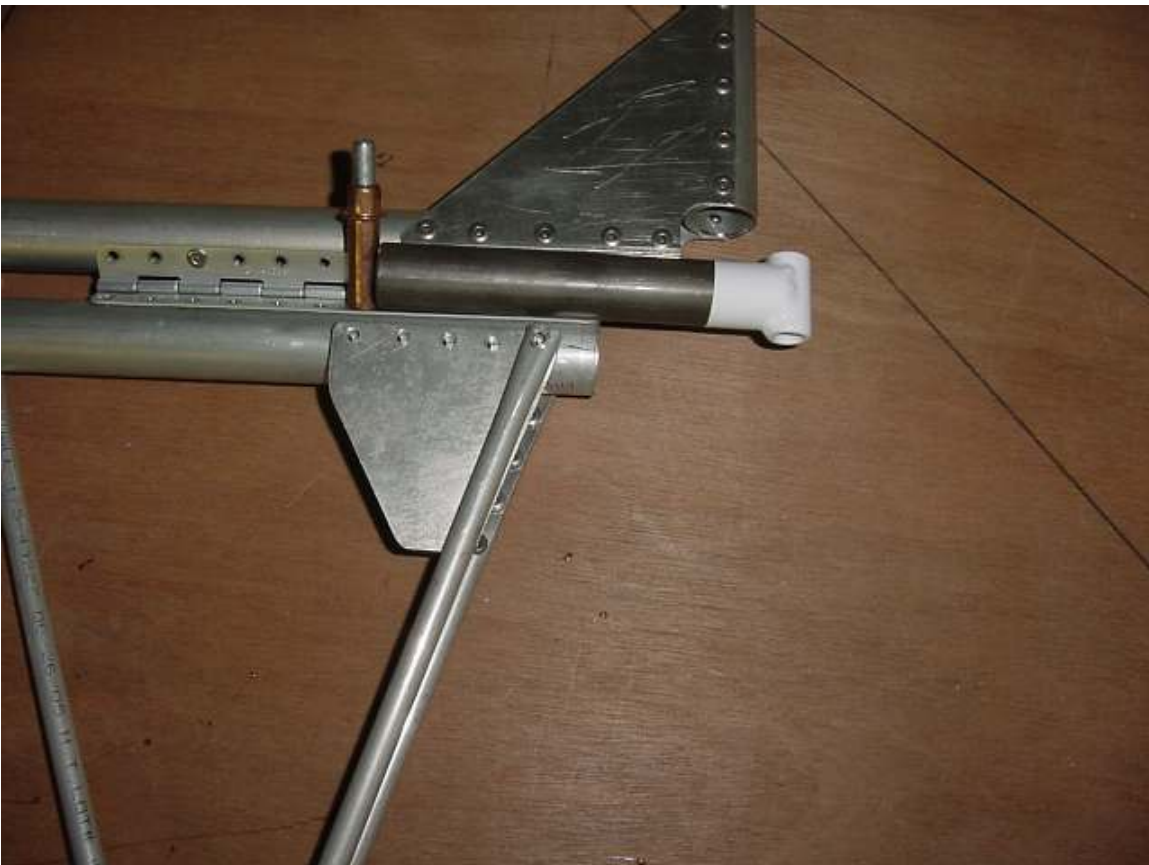

So we attempted to replace just the LE of the elevator but we are unhappy with the damage being done to the ribs from drilling out the rivets. I guess building new elevators is our best option. ☹

